



DEC Case# CO2-20110512-25, Modification to CO2-20000107-8

CSO Order on Consent  
**Quarterly Progress Report**  
**Second Quarter 2021**  
(April 1st – June 30<sup>th</sup>)

**July 31, 2021**

# Table of Contents

1. Executive Summary .....	3
2. Construction Contracts .....	9
3. Alley Creek CSO.....	11
4. Inner Harbor CSO.....	12
5. Flushing Bay CSO.....	13
6. Jamaica Tributaries CSO.....	16
7. Newtown Creek CSO .....	18
8. Westchester Creek CSO .....	21
9. Bronx River CSO.....	23
10. Hutchinson River CSO.....	24
11. Jamaica Bay CSO .....	25
12. Wards Island WRRF Headworks Wet Weather Improvements.....	29
13. Environmental Benefit Projects.....	31
14. Green Infrastructure Program.....	32
15. Community Relations .....	37
16. Key DEP Personnel.....	38
17. Overview of LTCP Program.....	39
18. Status of LTCP Development.....	41
19. LTCP Progress Update .....	44
20. Citywide/Open Waters LTCP Update.....	45



# 1. Executive Summary

---

*The City of New York (the “City”), the New York City Department of Environmental Protection (DEP), and the New York State Department of Environmental Conservation (DEC) entered into the Combined Sewer Overflow Order on Consent (DEC Case # CO2-20000107-8) on January 14, 2005, which was modified April 14, 2008, September 3, 2009, March 8, 2012, and March 26, 2015 (collectively, the “CSO Order”). Pursuant to the Order, the City is required to submit quarterly status reports to DEC (“Quarterly Reports”) describing actions taken toward achieving compliance with the Order during the prior three-month period.*

---

This Quarterly Report summarizes DEP’s actions and activities toward complying with the Order’s milestones between **April 1, 2021** and **June 30, 2021**. DEP continued to make progress in the planning, design, and construction of its CSO facilities during this quarter, as documented in this report. As required by the Order, DEP and DEC held a Quarterly Progress Meeting on **June 23, 2021** for the **first** quarter of **2021** and is scheduled to hold a Quarterly Progress Meeting on **September 29, 2021** to discuss issues related to the Order and review milestones met during the **second** quarter of 2021.

On March 19, 2020, DEP submitted a Notice of Force Majeure for the CSO Order due to the COVID-19 pandemic. DEP is monitoring for any related impacts to CSO Order milestones and to notify DEC in a timely manner in accordance with the terms of the CSO Order. Any delays or potential delays that have been identified are discussed in this report.

As a direct result of the economic impacts of COVID-19 on New York City finances and the ongoing uncertainty of long-term impacts, DEP continues to face multiple fiscal pressures including; a) Deferred spending for critical infrastructure projects from FY 2020; b) Projected potential fiscal impacts of COVID-19 and projected impacts to revenue; and c) DEP priority to maintain sufficient funding for critical infrastructure projects necessary for the ongoing operation and maintenance of the DEP’s water and wastewater treatment and conveyance systems, including the Wastewater Resource Recovery Facilities (WRRFs). Given the current fiscal uncertainty and projected potential reduction in revenue caused by COVID-19, DEP must seek to allocate budget resources to reflect expected revenue, balanced with the affordability of water rates for DEP ratepayers. In order to respond to these issues and responsibly allocate resources, DEP is engaged in an ongoing effort to evaluate funding for all projects in the current and upcoming fiscal years to prioritize projects critical to DEP’s core mission to provide clean drinking water and collect and treat wastewater during dry and wet weather to protect water quality in and around New York City in accordance with the regulatory requirements of the Safe Drinking Water Act and Clean Water Act. To the extent any funding constraints may impact future compliance

with the milestones covered in this Quarterly Report, DEP will notify DEC and make best efforts to mitigate any delays.

### Reportable Activity This Quarter

Date	Location	Event Description

### Milestone Actions This Quarter (April 1 – June 31, 2021)

Location	Item Description	Milestone Date	Action Required	Status
Citywide GI	4% GI Contingency Plan	June 30, 2021	Submission	DEP submitted a Contingency Plan.
Newtown Creek LTCP	Initiate Final Design	July 2021	Issue NTP	NTP Issued June 30, 2021

### Milestone Actions Next Quarter (July 1 – September 30, 2021)

Location	Item Description	Milestone Date	Action Required	Status

## Pending Modification Requests (MR) and Open Force Majeure Event Claims (FM)

Location	Item Description	Action(s)	Reason for Action(s)	Milestone Date	Status
Jamaica Bay	26 <sup>th</sup> Ward HLSS Phase II	<ul style="list-style-type: none"> <li>• DEP submitted FM 5/14/18</li> <li>• DEP provided additional info on 3/11/19</li> <li>• DEC acknowledged valid FM on 06/05/19</li> <li>• DEP submitted a Modification Request on 11/2/20</li> <li>• DEC response to Modification Request. DEC will use enforcement discretion.</li> <li>• DEP submitted FM related to COVID-19 delays on 3/19/20</li> <li>• DEC responded on 3/26/20 requested additional information</li> <li>• DEC acknowledged valid FM on 09/21/20</li> </ul>	<p>Force Majeure - NYCHA Steam pipe interferences</p> <p>Force Majeure - COVID-19 and related delays</p>	Dec 2020 (Construction Completion)	<p>DEC will exercise enforcement judgement until 6/30/2021.</p> <p>06/22/21 - DEP requested a new construction completion date of October 1, 2021.</p>
Jamaica Bay	26 <sup>th</sup> Ward HLSS Phase III	<ul style="list-style-type: none"> <li>• DEP submitted MR 3/1/19</li> <li>• DEP provided additional info on 8/14/19</li> <li>• DEP submitted a MR on 1/21/21</li> </ul>	Buckeye Fuel Pipe Interferences, Cover Issues	Mar 2019 (Design Completion)	DEP proposed to eliminate Phase III milestones due to interferences, costs and lack of WQ improvement

Location	Item Description	Action(s)	Reason for Action(s)	Milestone Date	Status
Bowery Bay/EROW	Area-wide ROW Green Infrastructure in BB-005 CSO Tributary Area	<ul style="list-style-type: none"> <li>• DEP submitted FM 6/26/19</li> <li>• DEP submitted extension request for informal negotiations on 1/29/21</li> <li>• DEC extended period for informal negotiations until 5/1/21.</li> </ul>	No awardable bids received	December 2020 (NTP)	DEC denied FM claim. DEP and DEC are in negotiations concerning the DEC determination.

Location	Item Description	Action(s)	Reason for Action(s)	Milestone Date	Status
Jamaica Bay	26 <sup>th</sup> Ward PSTs 1-5	<ul style="list-style-type: none"> <li>• DEP submitted FM on 12/20/19</li> <li>• DEC responded on 1/13/20 and requested additional information</li> <li>• DEP submitted additional information on 3/13/20</li> <li>• DEP submitted additional information on 9/11/20</li> <li>• DEC acknowledged FM to be valid on 10/9/20</li> <li>• DEP submitted an additional FM on 3/19/20</li> <li>• DEC responded on 3/26/20 requested additional information</li> <li>• DEP submitted additional information on 5/26/20</li> <li>• DEP updated the FM on 8/11/20</li> <li>• DEC acknowledged FM to be valid on 09/21/20</li> </ul>	<p>Force Majeure-deteriorated expansion joints in PST-4 and other PSTs</p> <p>Force Majeure - COVID-19 and related delays</p>	<p>Jan 2022 (Construction Completion)</p>	<p>On December 23, 2020, DEC approved an extension of 370 days for Appendix A, Milestone XII.C.9.</p>

Location	Item Description	Action(s)	Reason for Action(s)	Milestone Date	Status
Citywide GI	Certification of 2015 milestone (1.5%)	<ul style="list-style-type: none"> <li>• DEP submitted a mod request on 11/27/19</li> <li>• DEC responded on 12/10/19</li> <li>• DEP submitted a FM on 4/20/20.</li> <li>• DEC responded on 4/30/20.</li> <li>• DEP provided an additional update on 10/30/20.</li> </ul>	Force Majeure – COVID-19 and related delays	<del>December 31, 2019</del> December 31, 2020	Modified milestone will be needed due to FM. DEP intends to request a modification once the full extent of the delays has been identified.
All Locations	All open/active milestones	<ul style="list-style-type: none"> <li>• DEP submitted a FM notice on 3/19/20 for all active/open milestones</li> <li>• DEC responded to FM notice on 3/23/20 and requested further review in 60 days by DEP to assess impacts.</li> </ul>	Force Majeure COVID-19 - with potential delays due to ongoing pandemic	Multiple	Full extent of the delay has not yet been identified and DEP will keep DEC apprised on a project by project basis



## 2. Construction Contracts



The CSO Order contains milestones and schedules governing the planning, design and construction of DEP's Citywide CSO Program. Numerous CSO-related facilities will be constructed to reduce combined sewage discharges to the receiving waters surrounding the City. The table below identifies, by percentage, the estimated amount of construction that has been performed on projects that are in progress.

Location	Item Description	Notice to Proceed	Construction Completion Milestone	Projected Completion	% of Time Elapsed	% of Construction Completed <sup>(1)</sup>
Jamaica Bay Tributaries	Bergen Basin 18" Sanitary Sewer	Jan 2019	Oct 2021	Sept 2020	78%	100%
	26 <sup>th</sup> Ward HLSS Phase 1	Mar 2016	Dec 2018	Dec 2018	100%	100%
Jamaica Bay	26 <sup>th</sup> Ward HLSS Phase 2A	Sept 2017	Dec 2020	Jan 2021	100%	100%
	26 <sup>th</sup> Ward HLSS Phase 2B	Sept 2017	Dec 2020	Oct 2021	98%	99%

<b>Location</b>	<b>Item Description</b>	<b>Notice to Proceed</b>	<b>Construction Completion Milestone</b>	<b>Projected Completion</b>	<b>% of Time Elapsed</b>	<b>% of Construction Completed<sup>(1)</sup></b>
	<b>26<sup>th</sup> Ward HLSS Phase 3</b>	Mar 2020	Dec 2022	----	----	----
<b>Jamaica Bay</b>	<b>26<sup>th</sup> Ward PSTs 1-5</b>	Jan 2016	Jan 6, 2022	Jan 2022	<b>125.5%</b>	<b>88.9%</b>
	<b>Rockaway WRRF Conveyance</b>		Dec 2017	Pending Mod Request and negotiation resolution	-	-

(1) Percentage Construction Completion is tracked based on cost incurred.



### 3. Alley Creek CSO

**Alley Creek LTCP, Alley Creek CSO Retention Facility Disinfection System, Approved on March 7, 2017**

Design is on hold while DEP evaluates alternatives to disinfection based on additional facility planning for the disinfection facility. DEP intends to submit a modification request for the design completion milestone and likely subsequent milestones.

**Alley Creek CSO Schedule, CSO-AC-DF-DES**

<b>Alley Creek CSO</b>	<b>DEC Approved Milestones<sup>(1)</sup></b>	<b>Status</b>
1. Initiate Final Design	Sept 2018	Certified by DEP Oct 2, 2017
2. Design Completion	Sept 2021 <sup>(1)</sup>	BODR submitted to DEC Design on hold
3. Notice to Proceed to Construction	Sept 2022 <sup>(1)</sup>	TBD Pending Design Completion
4. Construction Completion	Sept 2024 <sup>(1)</sup>	TBD Pending Design Completion

<sup>(1)</sup> Milestone dates may be subject to revision by DEC based on additional facility planning.



## 4. Inner Harbor CSO

### **Gowanus Canal CSO LTCP Approved on March 29, 2017**

- February 27, 2015 - DEP certified construction completion of the Flushing Tunnel Modernization and Pump Station Reconstruction as of December 24, 2014 and June 20, 2014 respectively.
- April 13, 2015 – DEC accepted DEP’s certification of construction completion in accordance with the CSO Order.
- DEP continues to operate the Flushing Tunnel in accordance with its operational plan.
- DEP completed a project to mitigate foam from the Gowanus Canal Flushing tunnel as of January 3, 2020.





# 5. Flushing Bay CSO

The Flushing Bay CSO Facility Planning area includes the portions of the Tallman Island WRRF and the High Level Interceptor of the Bowery Bay WRRF drainage areas, associated sewers, and pumping stations that discharge to Flushing Bay and Flushing Creek in Queens.

## Construction Contracts

	Tallman Island Flushing Interceptor	Divert Low-Lying Sewers / Raise Weir BB-R02	Regulator Modifications	Environmental Dredging
<i>Contract ID</i>	TBD	CS-FB-LLD	CS-FB-BWR	CSO-DRDG DRG-FB
<b>Plan Elements</b>	Monitor Flushing Interceptor sag in Ulmer Street and address if periodic monitoring indicates necessity	Divert Low Lying sewers in vicinity of Bowery Bay WRRF. Raise weir at regulator BB-02	Bowery Bay High Level Interceptor regulator modifications at ten regulators	Environmental Dredging of Flushing Bay
<b>Location</b>	From MH 45 at Whitestone Expressway to MH 29 at Ulmer Street and 25 <sup>th</sup> Avenue	Regulator BB-02. Berrian Blvd and 19 <sup>th</sup> Ave between 43 <sup>rd</sup> St. and 45 <sup>th</sup> St.	Five of ten regulators along 108 <sup>th</sup> street, Ditmars Blvd and the LaGuardia Airport site	Proximate to CSO Outfalls BB-006 and BB-008
<b>Construction Cost</b>	TBD	\$5,610,000	\$28,959,345	\$37,560,000
<b>Status</b>	Next scheduled survey in 2022	Certified Complete on 9/11/2017	Certified Complete on 6/8/2018	Dredging Complete on 7/10/17 – Construction completed on 8/16/18. Currently in 2-year maintenance period.

## Design Activity Summary

	This Quarter	Next Quarter
<b>Divert Low-Lying Sewers / Raise Weir BB-R02</b>	<ul style="list-style-type: none"> <li>Complete</li> </ul>	
<b>Regulator Modifications</b>	<ul style="list-style-type: none"> <li>Complete</li> </ul>	

## Construction Activity Summary

	This Quarter	Next Quarter
<b>Divert Low-Lying Sewers / Raise Weir BB-R02</b>	<ul style="list-style-type: none"> <li>Certified completion on 9/11/2017</li> </ul>	
<b>Regulator Modifications</b>	<ul style="list-style-type: none"> <li>Certified completion on 6/8/2018</li> </ul>	
<b>Environmental Dredging</b>	<ul style="list-style-type: none"> <li>Certified completion on 8/16/2018. Continue with 2-year maintenance period</li> <li>DEC accepted Certificate of Construction Completion on 10/29/2018</li> </ul>	

**Flushing Bay LTCP, Flushing Bay 25 MG CSO Storage Tunnel, Approved on March 7, 2017**

**Flushing Bay CSO Schedule, CSO-FB-TUN**

<b>Flushing Bay CSO</b>	<b>DEC Approved Milestones<sup>(1)</sup></b>	<b>Status</b>
1. Initiate Final Design	Jul 2021	Force Majeure Submitted 9-16-20 – Delay Expected
2. Design Completion	Jun 2025	TBD Pending Design Start
3. Notice to Proceed to Construction	Jul 2026	TBD Pending Design Completion
4. Construction Completion	June 2035	TBD Pending Design Completion

<sup>(1)</sup> Milestone dates may be subject to revision by DEC based on additional facility planning.

**Flushing Creek LTCP, TI-010 Outfall Disinfection at CSO Retention Tank and Diversion Chamber 5, TI-011 Outfall Disinfection, Floatables Control at TI-R09 and Division Chamber 3, Approved on March 7, 2017**

**Flushing Creek CSO Schedule, CSO-FC-FB-DES**

<b>Flushing Creek CSO</b>	<b>DEC Approved Milestones<sup>(1)</sup></b>	<b>Status</b>
1. Initiate Final Design	Dec 2018	Certified by DEP on Feb 8, 2019
2. Design Completion	Sept 2022	Design in progress 30% design
3. Notice to Proceed to Construction	Sept 2023	TBD Pending Design Completion
4. Construction Completion	Dec 2025	TBD Pending Design Completion

<sup>(1)</sup> Milestone dates may be subject to revision by DEC based on additional facility planning.



## 6. Jamaica Tributaries CSO

*The Jamaica Tributaries CSO Facility Planning area includes the drainage area of the Jamaica WRRF and its associated sewers and pumping stations. The receiving waters of the study area are Bergen, Thurston, Shellbank, and Hawtree Basins, which are located along the eastern shore of Jamaica Bay on either side of JFK International Airport.*

### Construction Contracts

	<b>Parallel 48-inch Siphon / Interceptor</b>	<b>Bending Weirs</b>	<b>Bergen Basin 18" Sewer</b>
<i>Contract ID</i>	CS-JA-BBS	CS-JA-BWR	SEQ002714
<b>Plan Elements</b>	Parallel 48-inch Sewer	Bending Weirs	18-inch Sanitary Sewer
<b>Location</b>	Belt Parkway Queens	Regulator J6 on the East Interceptor and regulators J3 and J14 on the West Interceptor	150 <sup>th</sup> Ave between 126 and 129 Streets
<b>Construction Cost</b>	\$20,256,909	\$6,853,955	\$4,990,000
<b>Status</b>	Completed	Completed	In-Construction
<b>Other Issues</b>			



## Design Activity Summary

This Quarter		Next Quarter
Parallel 48-inch Siphon/Interceptor	<ul style="list-style-type: none"> <li>Complete</li> </ul>	
Bergen Basin 18" Sewer	<ul style="list-style-type: none"> <li>Complete</li> </ul>	

## Construction Activity Summary

This Quarter		Next Quarter
Parallel 48-inch Siphon/Interceptor	<ul style="list-style-type: none"> <li>Certified completion on 2/28/17</li> </ul>	
18-inch Sanitary Sewer in 150 <sup>th</sup> Avenue	<ul style="list-style-type: none"> <li>DEC accepted certification of completion on 7/6/20</li> </ul>	



## 7. Newtown Creek CSO

*The Newtown Creek CSO Facility Planning area includes the portions of the Newtown Creek WRRF and the Low Level Interceptor of the Bowery Bay WRRF drainage areas that discharge to Newtown Creek, English Kills, Dutch Kills, Whale Creek, Maspeth Creek and the East Branch along the Brooklyn-Queens border.*

### Construction Contracts

	<b>Enhanced Aeration 2</b>	<b>Bending Weirs / Floatables Control</b>
<b>Contract ID</b>	CSO-NC-3	CS-NC-REG & FLO
<b>Plan Elements</b>	Enhanced Aeration	Floatable Controls and Overflow Reduction
<b>Location</b>	East Branch and Upper Newtown Creek	Dutch Kills, Maspeth Creek, English Kills and East Branch
<b>Construction Cost</b>	\$16,704,250 (G+E+H Contract amounts together)	\$43,763,292
<b>Status</b>	Certified Complete – 6/9/18	Certified Complete – 11/22/2017
<b>Other Issues</b>		

## Design Activity Summary

	This Quarter	Next Quarter
<b>Enhanced Aeration 2</b>	<ul style="list-style-type: none"><li>• Complete</li></ul>	
<b>Bending Weirs / Floatables Control</b>	<ul style="list-style-type: none"><li>• Complete</li></ul>	

## Construction Activity Summary

	This Quarter	Next Quarter
<b>Enhanced Aeration 2</b>	<ul style="list-style-type: none"><li>• Complete</li></ul>	
<b>Bending Weirs / Floatables Control</b>	<ul style="list-style-type: none"><li>• DEP submitted Post Construction Monitoring on 8/19/2019</li></ul>	

**Newtown Creek LTCP, Borden Avenue Pump Station Expansion, 62.5% CSO Storage Tunnel, Approved on June 27, 2018**

**Newtown Creek CSO Schedule**

<b>Borden Ave Pumping Station Expansion</b>	<b>DEC Approved Milestones</b>	<b>Status</b>
1. Initiate Final Design	Jul 2021	<b>NTP Issued June 2021</b>
2. Design Completion	Dec 2024	TBD Pending Design Start
3. Notice to Proceed to Construction	Sept 2025	TBD Pending Design Completion
4. Construction Completion	Sep 2029	TBD Pending Design Completion

<b>CSO Storage Tunnel</b>	<b>DEC Approved Milestones</b>	<b>Status</b>
1. Initiate Final Design	Jun 2025	<b>DEP Procuring Contract</b>
2. Design Completion	May 2028	TBD Pending Design Start
3. Notice to Proceed to Construction	Aug 2030	TBD Pending Design Completion
4. Construction Completion	Jun 2042	TBD Pending Design Completion



## 8. Westchester Creek CSO

The Westchester Creek CSO Facility Planning area includes a portion of the Hunts Point WRRF drainage area, its associated sewers, and pumping stations that discharge to Westchester Creek and Pugsley Creek in the Bronx.

### Construction Contracts

	<b>Modifications to CSO-29 and CSO-29A</b>	<b>Pugsley Creek Parallel Interceptor Start from CSO-24</b>
<b>Contract ID</b>	CS-ER-WCM	CS-ER-WCP
<b>Plan Elements</b>	Improve flow control structures in sewers to convey more flow to the Hunts Point WRRF	Reduce CSO discharges to Pugsley Creek, which would otherwise <i>increase</i> because of the conveyance improvements at Eastchester Road
<b>Location</b>	Eastchester Road, Bronx	Classon Point, Bronx
<b>Construction Cost</b>	\$18.9 Million	\$85.1 Million
<b>Status</b>	Completed	Completed
<b>Other Issues</b>		

## Design Activity Summary

This Quarter		Next Quarter
Modifications to CSO-29 and CSO-29A	<ul style="list-style-type: none"> <li>Completed</li> </ul>	
Pugsley Creek Parallel Interceptor Start from CSO-24	<ul style="list-style-type: none"> <li>Completed</li> </ul>	

## Construction Activity Summary

This Quarter		Next Quarter
Modifications to CSO-29 and CSO-29A	<ul style="list-style-type: none"> <li>Completed</li> </ul>	
Pugsley Creek Parallel Interceptor Start from CSO-24	<ul style="list-style-type: none"> <li>Completed</li> </ul>	





## 9. Bronx River CSO

**Bronx River LTCP, Bronx River Hydraulic Relief at HP-007 and HP-009, Bending Weir and Baffle at HP-011, Approved on March 7, 2017**

### Bronx River CSO Schedule, CSO-BXR-DES

Bronx River CSO	DEC Approved Milestones <sup>(1)</sup>	Status
1. Initiate Final Design	Sept 2018	Design Initiated 8/27/2018
2. Design Completion	Sept 2022	DEP submitted modifications to design scope on 10/30/2020
3. Notice to Proceed to Construction	Sept 2023	TBD Pending Design Completion
4. Construction Completion	Sept 2026	TBD Pending Design Completion

<sup>(1)</sup> Milestone dates may be subject to revision by DEC based on additional facility planning.



# 10. Hutchinson River CSO

**Hutchinson River LTCP, CSO Outfall HP-024 Extension and Floatables Control Facilities, CSO Outfall HP-024 Extension Disinfection, Approved on March 7, 2017**

## Hutchinson River CSO Schedule, CSO-HR-DF-DES

Hutchinson River CSO	DEC Approved Milestones <sup>(1)</sup>	Status
1. Initiate Final Design, Extension and Floatables Control	Sept 2018	Design Initiated 8/15/2018
2. Design Completion	Sept 2022	DEP submitted to DEC modifications to design on 3/16/21
3. Notice to Proceed to Construction	Sept 2023	TBD Pending Design Completion
4. Construction Completion	Mar 2026	TBD Pending Design Completion
1. Initiate Final Design, Extension Disinfection	Sept 2022	Design Initiated 8/15/2018
2. Design Completion	Mar 2026	DEP submitted to DEC modifications to design on 3/16/21
3. Notice to Proceed to Construction	Mar 2027	TBD Pending Design Completion
4. Construction Completion	Mar 2030	TBD Pending Design Completion

<sup>(1)</sup> Milestone dates may be subject to revision by DEC based on additional facility planning.





# 11. Jamaica Bay CSO

*The Jamaica Bay CSO Facility Planning area includes the drainage areas of the 26<sup>th</sup> Ward, Coney Island, and Rockaway WRRFs and their associated sewers and pumping stations. The receiving waters of the study area include Fresh Creek, Hendrix Creek, Spring Creek, and the open waters of Jamaica Bay.*

## Construction Contracts

	Rockaway WWTP Conveyance Improvements	26 <sup>th</sup> Ward High Level Sewer Separation	26 <sup>th</sup> Ward Wet Weather Stabilization
<b>Contract ID</b>	Project not yet initiated	CS-FC-SEW	26W-12(CO 128) 26W-21, 26W-20
<b>Plan Elements</b>	Achieve 2xDDWF at WWTP	Remove storm water contribution from 285 acres from the combined sewer system	Low Level MSPs High Level MSPs PST#5 PST1-4 Stabilization
<b>Location</b>	Rockaway WWTP, Queens	Fresh Creek, Brooklyn	26 <sup>th</sup> Ward WWTP, Brooklyn
<b>Construction Cost</b>	TBD	\$58 million for Phase 1A; \$90.6 million for Phases 2A and 2B; 235.5 million for Phases 3A and 3B (estimated)	LLMSP \$7.6 million 26W-21 \$17.3 million 26W-20 <b>\$153</b> million
<b>Status</b>	RK sewer system maximizes wet weather flow to WRRF. Project not yet initiated. In discussions with DEC.	Phase 1A construction completed, with variance from approved design Phase 2 is in construction Phase 3 design is paused pending engineering evaluation and analysis of the impacts of	Completed (LLMSPs) Completed (26W-21) In Construction (26W-20)

	eliminating the Phase 3 component of the project.
<b>Other Issues</b>	<p>For Phase 2B (SE855): NYCHA steam pipes were discovered during construction that interfere with storm/high level storm sewers in four locations. DEP and DDC hired consultant to perform design for NYCHA steam pipes offset. For Phase 3A (SE856): it was previously identified interferences with Buckeye Pipelines in four locations. Preliminary design around Buckeye Fuel Lines is prepared by DDC and submitted to Buckeye Partners, L.P. Buckeye requested that DDC include their existing utility locations on the design drawings. DEP review of the preliminary design drawings is complete. DDC is incorporating DEP comments and will then submit revised drawings for Buckeye review. For Phase 3B (SE857): low cover issues have been addressed and a preliminary design review has been completed by DEP.</p>

## Design Activity Summary

	This Quarter	Next Quarter
<b>26<sup>th</sup> Ward High Level Sewer Separation</b>	<ul style="list-style-type: none"> <li>Design for Phase 2B to resolve NYCHA Steam Pipe Interferences was approved by all involved parties.</li> <li>Design of Phase 3 is cancelled following DEC acknowledgement of project Cancellation on 6/3/2021</li> </ul>	
<b>26<sup>th</sup> Ward Preliminary Treatment Reliability Improvements</b>	<ul style="list-style-type: none"> <li>Continued DSDC</li> </ul>	<ul style="list-style-type: none"> <li>Continuation of DSDC</li> </ul>

## Construction Activity Summary

	This Quarter	Next Quarter
26 <sup>th</sup> Ward High Level Sewer Separation	<ul style="list-style-type: none"> <li>Phase 2A (SE853)</li> <li>Completed work in Q2:               <ul style="list-style-type: none"> <li>This portion of Phase II is substantially complete.</li> <li>Complete Final Inspection Checklist</li> </ul> </li> </ul> <p>Phase 2B (SE855)</p> <ul style="list-style-type: none"> <li>DDC Completed the design of the NYCHA Steam Pipes at all four locations and has been approved by all parties involved.</li> <li>Contractor began working on NYCHA Steam Pipe Crossings.</li> <li>DEC has acknowledged the mod request sent by DEP. The new Construction Completion Milestone is 9/30/2021.</li> </ul>	<p>Phase 2A (SE853)</p> <ul style="list-style-type: none"> <li>Provide DEP with substantial Completion Letter</li> </ul> <p>Phase 2B (SE855)</p> <ul style="list-style-type: none"> <li>Contractor is expected to continue construction and substantially complete the sewer by 9/30/2021.</li> </ul>
26 <sup>th</sup> Ward Preliminary Treatment Reliability Improvements	<p>PST work (26W-20):</p> <ul style="list-style-type: none"> <li>Completed rehabilitation of expansion joints under Change Order# 103, construction of concrete structures, and installation of sludge collector system in PST-2.</li> <li>Completed effluent channel precast slabs, scum troughs, influent box, and sludge collector system for PST-2. Completed dry run of flights in PST-2.</li> <li>Continued demolition and rehabilitation of expansion joint (CO-103 work) in PST-1 including rebuilding the concrete joint face at all</li> </ul>	<p>PST work (26W-20):</p> <ul style="list-style-type: none"> <li>Perform clean water leak test in PST-2. Bring PST-2 successfully online with sewage.</li> <li>CO-103 work: Complete rehabilitation of expansion joints in PST-1 and epoxy coating of PST-1.</li> <li>Complete PST-1 concrete rehabilitation work. Complete installation of collector system equipment. Perform dry run, clean water test, and</li> </ul>

This Quarter	Next Quarter
<p>expansion joint locations (<b>work is 85% complete</b>). Continued PST-1 concrete rehabilitation and installation of sludge collector system. Started construction of effluent troughs and scum troughs. Demolished PST-1 influent channel and <b>constructed new PST-1 influent box.</b></p> <ul style="list-style-type: none"> <li>• <b>Remove existing sludge pumps #1, 2, and 3 and start installation of the replacement pumps.</b></li> <li>• <b>Demolished PSG West Entrance Building and Existing Splitter Box.</b></li> <li>• <b>Installed and completed concrete encasement of 48" Raw Sewage Pipe</b></li> <li>• <b>Completed 2nd floor Supervisor's Personnel area work.</b></li> <li>• <b>Completed installation of conduits and wire to GTP flowmeter in MV-2.</b></li> <li>• <b>Completed installation of permanent 78" FM pipe and demolition of temporary system.</b></li> <li>• <b>Start construction of West Stair at PSG.</b></li> </ul>	<p><b>successfully bring PST-1 online.</b></p> <ul style="list-style-type: none"> <li>• <b>Complete 48" RS piping to PST-1.</b></li> <li>• <b>Complete installation of West Stairs at PSG.</b></li> <li>• <b>Complete installation of new Sludge Pumps #1, 2, and 3 in PSG including power and controls.</b></li> <li>• <b>Complete sludge piping, flushing water piping, and seal water piping in PSG.</b></li> <li>• <b>Complete PST walkways and handrails.</b></li> <li>• <b>Complete asphalt paving of Plant roads.</b></li> </ul>



# 12. Wards Island WRRF Headworks Wet Weather Improvements

*The Wards Island WRRF Headworks Wet Weather Improvements consist of work done at the WRRF to increase its wet weather handling capacity. The projects described in this section 3.7 were added to the 2012 CSO Order through a modification effective March 26, 2015 (DEC Case No. CO2-20140314-01).*

## Construction Contracts

	<b>MSP Reconstruction</b>	<b>Bar Screen Replacement</b>
<b>Contract ID</b>	WI - 288(R)	WI – 280
<b>Plan Elements</b>	Reconstruction of Six (6) MSPs	Replace Bar Screens at Bronx and Manhattan Grit Chambers
<b>Location</b>	Wards Island WRRF	Wards Island WRRF
<b>Status</b>	Completed	Completed
<b>Construction Cost</b>	\$5,292,653	\$13,715,000
<b>Other Issues</b>	None	None

**Design Activity Summary**

This Quarter		Next Quarter
MSP Replacement	<ul style="list-style-type: none"> <li>• Complete</li> </ul>	
Bar Screen Replacement	<ul style="list-style-type: none"> <li>• Complete</li> </ul>	

**Construction Activity Summary**

This Quarter		Next Quarter
MSP Replacement	<ul style="list-style-type: none"> <li>• Completed reconstruction of the 6<sup>th</sup> MSP (MSP#3 on July 24, 2019)</li> </ul>	<ul style="list-style-type: none"> <li>• DEC inspection of replacement work</li> </ul>





## 13. Environmental Benefit Projects

---

*DEP has undertaken these projects in connection with the settlement of a New York State and DEC enforcement action. The Environmental Benefit Projects (EBPs) are funded by DEP and designed to abate CSOs and/or address wet weather water quality impacts from CSOs and to benefit the waters in and around New York City.*

---

The 2008 modifications to the CSO Consent Order require not less than \$4 million worth of DEP-funded Environmental Benefit Projects (EBPs) designed to abate CSOs and/or address wet weather water quality impacts from CSOs and to benefit the waters in and around New York City. In addition to the EBPs, the 2012 Order requires that \$2 million in EBP funding be allocated toward the Hutchinson River and Newtown Creek Neighborhood Demonstration Areas. That funding commitment was met and the Demonstration Area projects are now complete.

DEP completed monitoring for all six EBPs and has disbursed all payments to the EBP grantees. In November 2020, DEP submitted all close-out materials for the EBPs to DEC. On December 1, 2020, DEC confirmed receipt of the close-out materials. On December 14, 2020, the final grantee payment was received.





# 14. Green Infrastructure Program

*The 2012 CSO Consent Order sets forth schedule and stormwater capture targets and other requirements for the program to reduce CSO volume through the use of green infrastructure.*

## Program Implementation

DEP has identified Priority Areas based on several criteria, such as annual CSO volume, frequency of CSO events, and projected benefits of projects constructed through DEP's Waterbody/Watershed Facility Plans or other system improvements planned. DEP also notes outfalls in close proximity to existing and future public access locations. DEP continues to review and expand the Priority Areas to ensure sufficient green infrastructure implementation to meet the 2030 goal set forth in the Order.

The identification of Priority Areas has enabled DEP to focus resources on specific CSO tributary areas, to analyze all potential opportunities, to saturate these areas with green infrastructure as much as possible, and to achieve efficiencies in design and construction.

DEP has initially focused primarily on the Area-wide right-of-way contracts building curbside rain gardens, infiltration basins, Stormwater Greenstreets, and porous paving. DEP's standardized designs and procedures have been critical to supporting the systematic implementation of green infrastructure at a wide scale. DEP expects to continue green infrastructure implementation using an expanded array of tools. While right-of-way implementation has been the greatest focus of the first decade of the Program, DEP is making significant advancements into other implementation areas as well,



**Curbside Rain Garden (Bioswale)**



**Stormwater Greenstreet**



expanding public on-site retrofits on schools, parks and housing properties, advancing new stormwater regulations, exploring daylighting opportunities in the Bronx, and implementing stormwater recovery and reuse projects.

During the **Second Quarter of 2021**, planning, design and construction work continued in several Green Infrastructure (GI) Program initiatives and are generally summarized below.

- ROW - Ongoing Area-wide GI contracts to design and build thousands of curbside rain gardens, infiltration basins, stormwater greenstreets, and porous pavements in NYC's streets and sidewalks. Design and construction contracts are being implemented in multiple phases.
- Public Property Retrofits - Ongoing siting, design and construction of public property retrofits in coordination with City agency and non-profit partners.
- Green Infrastructure Grant Program - Ongoing design and construction of GI Grant Program projects on private property.
- Private Incentives Retrofit Program - Launch of the new private property retrofit program through which DEP seeks to implement green infrastructure to manage 200 greened acres over five years.
- Large-scale Street Medians - Ongoing siting and design by DEP's in-house green infrastructure design team, which focuses on large-volume capture opportunities within public medians with the added benefit of localized flooding alleviation
- Stormwater Reduction & Reuse – Ongoing design for Central Park and Prospect Park stormwater reuse projects that reduce potable demand and CSOs
- Tibbetts Brook and Van Cortlandt Lake Park Improvements – Ongoing planning and analysis for Tibbetts Brook daylighting project, anticipated to be the Program's largest green infrastructure project to-date providing significant CSO reduction and community benefits
- Unified Stormwater Rule – Ongoing planning, outreach and drafting of Unified Stormwater Rule to update and align Chapters 31 and 19.1 of Title 15 of the Rules of the City of



**Playground Retrofit**



**Porous Pavement – Queens College  
Green Infrastructure Grant Program**

New York (RCNY) and forthcoming New York City Stormwater manual.

## Status of Green Infrastructure Assets and Greened Acres

Watershed	Total Green Infrastructure Assets	Total Greened Acres
Alley Creek	1	0
Bronx River	446	93
Coney Island Creek	49	9
East River / Open Waters	1,118	195
Flushing Bay	772	82
Flushing Creek	1,879	196
Gowanus Canal	127	23
Hutchinson River	208	41
Jamaica Bay & Tributaries	4,634	559
Newtown Creek	1,586	163
Westchester Creek	230	23
<b>Total</b>	<b>11,050</b>	<b>1,504</b>

## Status of Green Infrastructure 1.5% Contingency Plan Projects<sup>1</sup>

Waterbodies	Area-Wide ROW Project	Status as of June 30, 2021		Reported Completion Date [1]	Projected/Actual Completion Date as of June 2021
		Number of Bids	Issued/Anticipated NTP Date		
Flushing Creek	TI-011	Construction Bid 1	Jun-16	Dec-19	Jun-17
		Construction Bid 2	Sep-18		Jun-20
Newtown Creek	BB Cluster	Construction Bid 1	Jan-17	Dec-19	Mar-19
		Construction Bid 2	Aug-19		Dec-20
Jamaica Bay	JAM-003	Construction Bid 1	Aug-16	Dec-19	Dec-17
		Construction Bid 2	Jan-19		Jul-20
		Construction Bid 3	Jul-19		Jun-20
		Construction Bid 4	Dec-20		Jun-22
		Construction Bid 5	Dec-19		Apr-21
EROW/Wallabout	NCB-014	Construction Bid 1	Sep-18	Dec-20	Dec-19
		Construction Bid 2	Dec-19		Jul-21
EROW/Bowery Bay	BB-005	Construction Bid 1	TBD	Dec-20	TBD
		Construction Bid 2	May-21		May-23
Westchester Creek	HP-014/033/016	Construction Bid 1	Jul-19	Dec-20	Dec-20
		Construction Bid 2	Jul-19		
Flushing Creek	TI-010	Construction Bid 1	Sep-19	Dec-20	Dec-20
		Construction Bid 2	Mar-21		Sep-22
		Construction Bid 3	Dec-19		Dec-21
		Construction Bid 4	Dec-19		Dec-21
		Construction Bid 5	Jun-20		Dec-21
		Construction Bid 6	Dec-19		Apr-21
Bronx River	HP-007/004/002	Construction Bid 1	Nov-19	Dec-20	Dec-20
		Construction Bid 2	Nov-19		Dec-20
Jamaica Bay	26W-005/004	Construction Bid 1	Dec-19	Dec-20	Dec-20

<sup>1</sup> The information in the above Table is correct as of January 22, 2021.

	Construction Bid 2	Dec-19		Dec-20
	Construction Bid 3	Dec-19		Dec-20
	Construction Bid 4	Dec-19		Dec-20
	Construction Bid 5	Dec-19		Dec-20

[1] The Anticipated Construction Completion date as reported in the June 27, 2016 Contingency Plan



## 15. Community Relations

*\*Public Participation Plan meeting photo taken prior to 3/2020, pre-COVID-19 distancing requirements.*

---

*DEP's Public Participation Plan was released to the public on June 26, 2012 and describes the multi-pronged tools and activities DEP will utilize to inform and involve diverse stakeholders and the broader public throughout the LTCP process. The Plan provides a framework for communicating with and soliciting input from interested stakeholders on water quality and the challenges and opportunities for CSO controls.*

---

DEP will report quarterly to DEC on completed public participation activities outlined in the public participation plan as part of this and all future CSO Quarterly Reports. All updates to the Public Participation Plan implemented as a result of public comments received and quarterly reviews of public participation activities by DEC will be posted annually to DEP's website.

### **LTCP and Green Infrastructure Education & Outreach Meetings**

DEP held a Green Infrastructure Grant workshop on June 9<sup>th</sup> with 69 people in attendance.

Updates on the LTCP Program including the submission of the Open Waters/Citywide LTCP are being shared with the public through the DEP website at [nyc.gov/dep/ltcp](http://nyc.gov/dep/ltcp).





# 16. Key DEP Personnel

Planning Area	Project	DEP Responsible Personnel		
		Bureau	PM	AM
Alley Creek	CSO-AC-DF-DES: Alley Creek CSO Disinfection	BEDC	Osit	Romano
Inner Harbor	CSO-GC: Flushing Tunnel	BEDC	Clarke	Eden
	CSO-GC: Gowanus PS	BEDC	Clarke	Joseph
Flushing Bay	CSO-DRDG: Dredging	BEDC	Tysvaer	Sewgobind
	CS-FB-LLD: Low-Lying Sewers	BWSO	Gordon	Dopson
	CS-FB-LLD R2 Weir	BWT	TBD	TBD
	CS-FB-BWR: Regulators	BEDC	Tysvaer	Gordon
	CSO-FC-FB-DES: Flushing CSO Floatables Control	BEDC	Tysvaer	Betemit
	CSO-FC-DF-DES: Flushing CSO Disinfection Facility	BEDC	Tysvaer	Betemit
	CSO-FB-TUN: Flushing Bay CSO Storage Tunnel	BEDC	Osit	Liu
Jamaica Tributaries	18" Sanitary Sewer in 150th Avenue	BWSO	Gordon	Dopson
Newtown Creek	CSO-NC-4: Dutch Kills, Lower Newtown	BEDC	Tysvaer	Ekhlas
	CSO-NC-3: East Branch, Upper Newtown	BEDC	Tysvaer	Ekhlas
	CSO-NC-2: Enhanced Aeration Lower English Kills	BEDC	Tysvaer	Adabi
	CS-NC-REG&FLO: Regulators / Floatables Control	BEDC	Tysvaer	Ekhlas
Westchester Creek	CS-ER-WCM: Modifications to CSO-29 / 29A	BEDC	Tysvaer	Betemit
	CS-ER-WCP: Pugsley Creek Parallel Interceptor	BWSO	Proscia	DeGrace
Bronx River	CSO-BXR-DES: Bronx River LTCP	BEDC	Solimando	Sadat
Hutchinson River	CSO-HR-DF-DES: Hutchinson River Disinfection	BEDC	Tysvaer	Szeto
Jamaica Bay	CS-FB-SEW: 26th Ward / Fresh Creek HLSS	BWSO	Gordon	Dopson
	26W-20: 26th Ward Wet Weather Stabilization	BEDC	Solimando	Heim
	26W-21: 26th Ward High Level MSPs	BEDC	Solimando	Heim
Wards Island	Reconstruction of MSP	BWT	Anderson	Anderson
EBP	Environmental Benefit Projects	BEPA	McLaughlin	Chen
GI	Green Infrastructure	BEPA	Enoch	Kocovic



# 17. Overview of LTCP Program

*The goal of each Long-Term Control Plan (LTCP) is to identify appropriate CSO controls necessary to achieve waterbody-specific quality standards, consistent with EPA's 1994 CSO Policy and subsequent guidance.*

## LTCP Milestones

	<b>CSO Watershed</b>	<b>LTCP Milestone</b>	<b>Status</b>
1	Alley Creek	June 2013	Approved 3/7/17
2	Westchester Creek	June 2014	Approved 8/1/17
3	Hutchinson River	September 2014	Approved 3/7/17
4	Flushing Creek	December 2014	Approved 3/7/17
5	Bronx River	June 2015	Approved 3/7/17
6	Gowanus Canal	June 2015	Approved 3/29/17
7	Coney Island Creek	June 2016	Approved 4/4/18
8	Flushing Bay	December 2016	Approved 3/7/17
9	Newtown Creek	June 2017	Approved 6/27/18
10	Jamaica Tributaries & Bay <sup>1</sup>	June 2018	DEC provided supplemental comments document 10/11/19
11	Citywide/Open Waters <sup>2</sup>	May 2020	<b>DEC Review</b>

1) Citywide/Open Waters include Harlem River, Hudson River, East River, and Upper and Lower New York Bay. Modification Request for extension of Citywide/Open Waters LTCP to December 31, 2018 approved by DEC on June 27, 2017.

2) Additional Modification Request for an extension of Citywide/Open Waters LTCP to May 30, 2020 approved by DEC on March 23, 2020.



# New York City CSO Watersheds

1







# 18. Status of LTCP Development

*The status of all Long-Term Control Plan development is described below.  
All Waterbody/Watershed Facility Plans (WWFPs) have been approved.*

## LTCP Activity Status

CSO Watershed	Alley Creek <sup>1</sup>	Westchester Creek <sup>2</sup>	Hutchinson River <sup>3</sup>	Flushing Creek <sup>4</sup>	Bronx River <sup>5</sup>	Gowanus Canal <sup>6</sup>	Coney Island <sup>7</sup>	Flushing Bay <sup>8</sup>	Newtown Creek <sup>9</sup>	Jamaica Bay <sup>10</sup>	Citywide/ Open Waters
LTCP Due Date	June 2013	Jun 2014	Sept 2014	Dec 2014	Jun 2015	Jun 2015	Jun 2016	Dec 2016	Jun 2017	Jun 2018	May 2020
Waterbody Startup											
Sampling											
Modeling											
Alternatives Development											
LTCP Development											
Public Participation											
Approval Date	Mar 2017	Aug 2017	Mar 2017	Mar 2017	Mar 2017	Mar 2017	Apr 2018	Mar 2017	Jun 2018	Pending	Pending

**LEGEND:** = Completed = In Progress = Not Initiated

<sup>1</sup>Final Alley Creek LTCP previously submitted to DEC June 30, 2013. Received DEC Determination Letter in December 12, 2013. DEP filed Article 78 proceeding on February 21, 2014. LTCP resubmitted to DEC on June 30, 2014. DEC Comments Letter received January 23, 2015. Supplemental Documentation submitted May 6, 2015.

<sup>2</sup>Final Westchester Creek LTCP submitted to DEC in June 30, 2014. DEC Comments Letter received September 22, 2014. Response Letter submitted November 24, 2014. Additional DEC Comments Letter received January 14, 2015. Response Letter and Supplemental Documentation submitted April 14, 2015. DEC Comment Letter received June 6, 2017. Response Letter submitted July 11, 2017.

<sup>3</sup>Final Hutchinson River LTCP submitted to DEC in September 30, 2014. DEC Comments Letter received January 14, 2015. Supplemental Documentation submitted April 14, 2015.

<sup>4</sup>Final Flushing Creek LTCP submitted to DEC in December 30, 2014. DEC Comments Letter received January 23, 2015. Supplemental Documentation submitted May 22, 2015.

<sup>5</sup>Final Bronx River LTCP submitted to DEC in June 30, 2015. DEC Comments Letter received August 24, 2015. Supplemental Documentation submitted September 23, 2015.

<sup>6</sup>Final Gowanus Canal LTCP submitted to DEC in June 30, 2015. DEC Comments Letter received August 5, 2015. Supplemental Documentation submitted September 8, 2015.


<sup>7</sup>Final Coney Island Creek LTCP submitted to DEC in June 30, 2016. DEC Comments Letter received August 17, 2016. Response Letter submitted September 16, 2016. DEC Comments Letter received April 6, 2017. Response Letter submitted October 2, 2017. DEP issued letter to DEC on December 5, 2017 based on discussions during October 18, 2017 DEC/DEP Technical Meeting. DEC Comments Letter received December 8, 2017. DEP submitted response letter on February 2, 2018.

<sup>8</sup>Final Flushing Bay LTCP submitted to DEC in December 31, 2016.

<sup>9</sup>Final Newtown Creek LTCP submitted to DEC in June 30, 2017. DEC Comments Letter received November 4, 2017. DEP submitted response letter January 8, 2018.

<sup>10</sup>Jamaica Bay and Tributaries LTCP submitted June 30, 2018. DEC Comment Letter dated December 21, 2018. Response Letter submitted March 1, 2019. Supplemental Documentation submitted August 14, 2019. DEC Comment Letter dated October 11, 2019.

# LTCP Work Plan Flow Chart

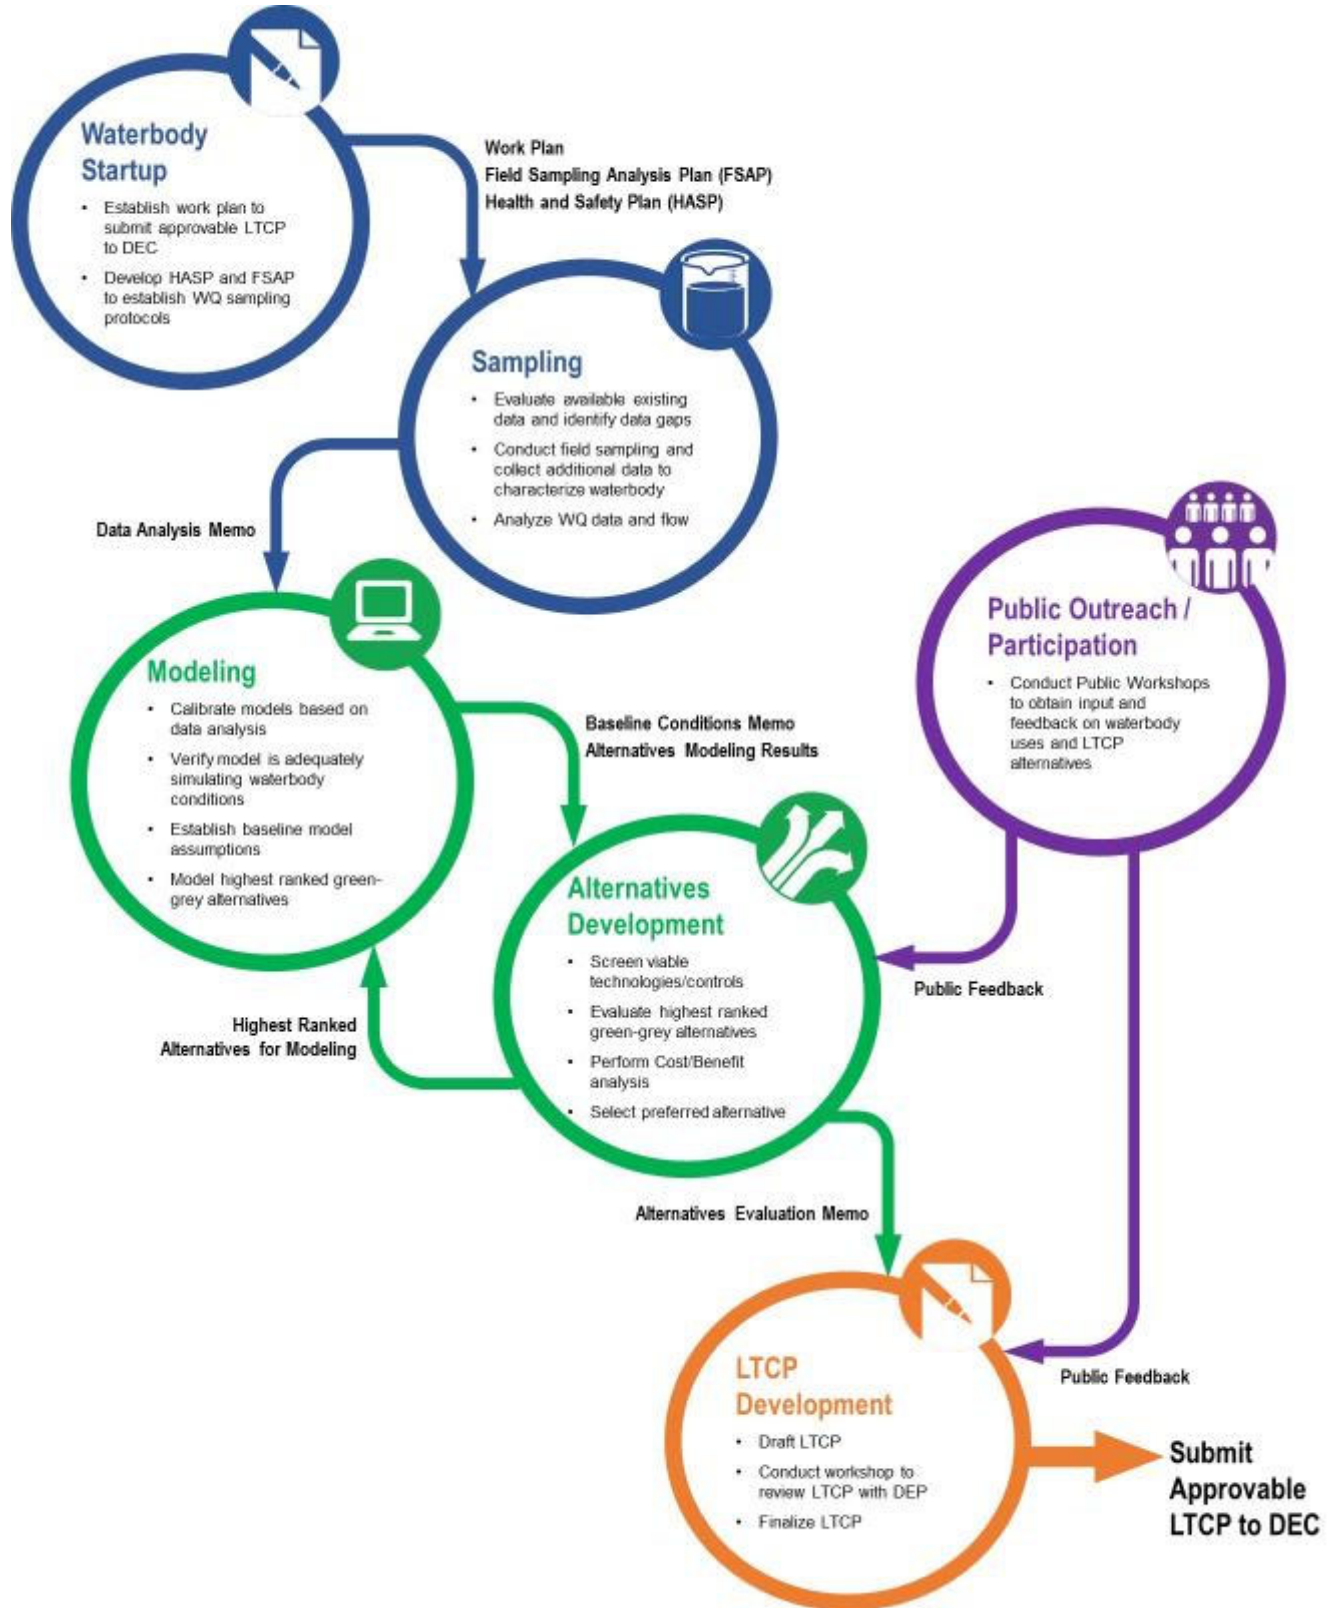



# 19. LTCP Progress Update

All LTCPs have either been approved or are under DEC review.





## 20. Citywide/Open Waters LTCP Update

DEP submitted the Citywide/Open Waters LTCP on September 30, 2020.
