

Hamilton Avenue Marine Transfer Station


DRAFT

ID	Task Name	Duration	Start	Finish	2006												2007												2008											
					D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J					
1	Hamilton MTS Notice To Proceed	610 days	Mon 1/2/06	Fri 5/2/08																																				
2	Contractor Mobilization	15 days	Mon 1/2/06	Fri 1/20/06																																				
3	Apply for Permits	5 days	Mon 1/2/06	Fri 1/6/06																																				
4	Obtain Permits	10 days	Mon 1/9/06	Fri 1/20/06																																				
5	Survey/Layout Site	5 days	Mon 1/2/06	Fri 1/6/06																																				
6	Mobilize trailer(s) to site	10 days	Mon 1/2/06	Fri 1/13/06																																				
7	Environmental Remediation	35 days	Mon 1/2/06	Fri 2/17/06																																				
8	Submit & Approve Remediation Shop Drawings	20 days	Mon 1/2/06	Fri 1/27/06																																				
9	Lead Abatement	15 days	Mon 1/30/06	Fri 2/17/06																																				
10	Asbestos Abatement	15 days	Mon 1/30/06	Fri 2/17/06																																				
11	Arsenic Abatement	15 days	Mon 1/30/06	Fri 2/17/06																																				
12	Dredging	85 days	Mon 1/2/06	Fri 4/28/06																																				
13	Submit & Approve Dredging Plan	20 days	Mon 1/2/06	Fri 1/27/06																																				
14	Complete Dredging	65 days	Mon 1/30/06	Fri 4/28/06																																				
15	Demolition of Existing Incinerator Building	120 days	Mon 1/2/06	Fri 6/16/06																																				
16	Submit & Approve Demolition Shop Drawings	30 days	Mon 1/2/06	Fri 2/10/06																																				
17	Demolition and Removal Building	20 days	Mon 2/20/06	Fri 3/17/06																																				
18	Demolition and Removal Concrete	40 days	Mon 3/20/06	Fri 5/12/06																																				
19	Survey Piles	10 days	Mon 5/15/06	Fri 5/26/06																																				
20	Remove or Cut Offshore Piles	15 days	Mon 5/29/06	Fri 6/16/06																																				
21	Pile Foundations	95 days	Mon 6/19/06	Fri 10/27/06																																				
22	Drive Piles	45 days	Mon 6/19/06	Fri 8/18/06																																				
23	Reinforced Concrete - Pile Caps and Beams	50 days	Mon 8/21/06	Fri 10/27/06																																				
24	Structural Concrete	140 days	Mon 10/30/06	Fri 5/11/07																																				
25	Reinforced Concrete Deck	45 days	Mon 10/30/06	Fri 12/29/06																																				
26	Reinforced Concrete Walls	30 days	Mon 2/26/07	Fri 4/6/07																																				
27	Reinforced Concrete Elevated Slab	30 days	Mon 3/19/07	Fri 4/27/07																																				
28	Concrete Encase Columns	50 days	Mon 3/5/07	Fri 5/11/07																																				
29	Structural Steel Building	110 days	Mon 12/11/06	Fri 5/11/07																																				
30	Floor and Misc. Framing	35 days	Mon 12/11/06	Fri 1/26/07																																				
31	Roof Framing	25 days	Mon 1/29/07	Fri 3/2/07																																				
32	Truss and Monitor Framing	20 days	Mon 1/29/07	Fri 2/23/07																																				
33	1/2" Steel Plate Push Wall Armor	20 days	Mon 2/26/07	Fri 3/23/07																																				
34	Steel Roof Deck	25 days	Mon 3/5/07	Fri 4/6/07																																				

Hamilton Avenue Marine Transfer Station						DRAFT																													
ID	Task Name	Duration	Start	Finish																															
					2006					2007					2008																				
					D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J
35	Steel Siding	25 days	Mon 4/9/07	Fri 5/11/07																															
36	Architectural	120 days	Mon 2/26/07	Fri 8/10/07																															
37	Masonry	25 days	Mon 2/26/07	Fri 3/30/07																															
38	Doors and Windows	30 days	Mon 4/23/07	Fri 6/1/07																															
39	Finishes	65 days	Mon 5/14/07	Fri 8/10/07																															
40	HVAC	120 days	Mon 5/14/07	Fri 10/26/07																															
41	Odor Control System	120 days	Mon 5/14/07	Fri 10/26/07																															
42	Dust Suppression System	120 days	Mon 5/14/07	Fri 10/26/07																															
43	Heating and Ventilating Equipment	120 days	Mon 5/14/07	Fri 10/26/07																															
44	Plumbing	80 days	Mon 5/14/07	Fri 8/31/07																															
45	Piping and Insulation	40 days	Mon 5/14/07	Fri 7/6/07																															
46	Plumbing Equipment and Fixtures	40 days	Mon 7/9/07	Fri 8/31/07																															
47	Fire Protection	80 days	Mon 5/14/07	Fri 8/31/07																															
48	Piping	40 days	Mon 5/14/07	Fri 7/6/07																															
49	Equipment	40 days	Mon 7/9/07	Fri 8/31/07																															
50	Electrical	140 days	Mon 5/14/07	Fri 11/23/07																															
51	MCC/Switchgear Installation	80 days	Mon 5/14/07	Fri 8/31/07																															
52	Interior Electrical Rough-in	80 days	Mon 5/14/07	Fri 8/31/07																															
53	Interior Wire and Cable	40 days	Mon 9/3/07	Fri 10/26/07																															
54	Interior Electrical Fixtures	20 days	Mon 10/29/07	Fri 11/23/07																															
55	Site Power and Lighting	80 days	Mon 5/14/07	Fri 8/31/07																															
56	Security System	60 days	Mon 9/3/07																																

Southwest Brooklyn Marine Transfer Station

DRAFT

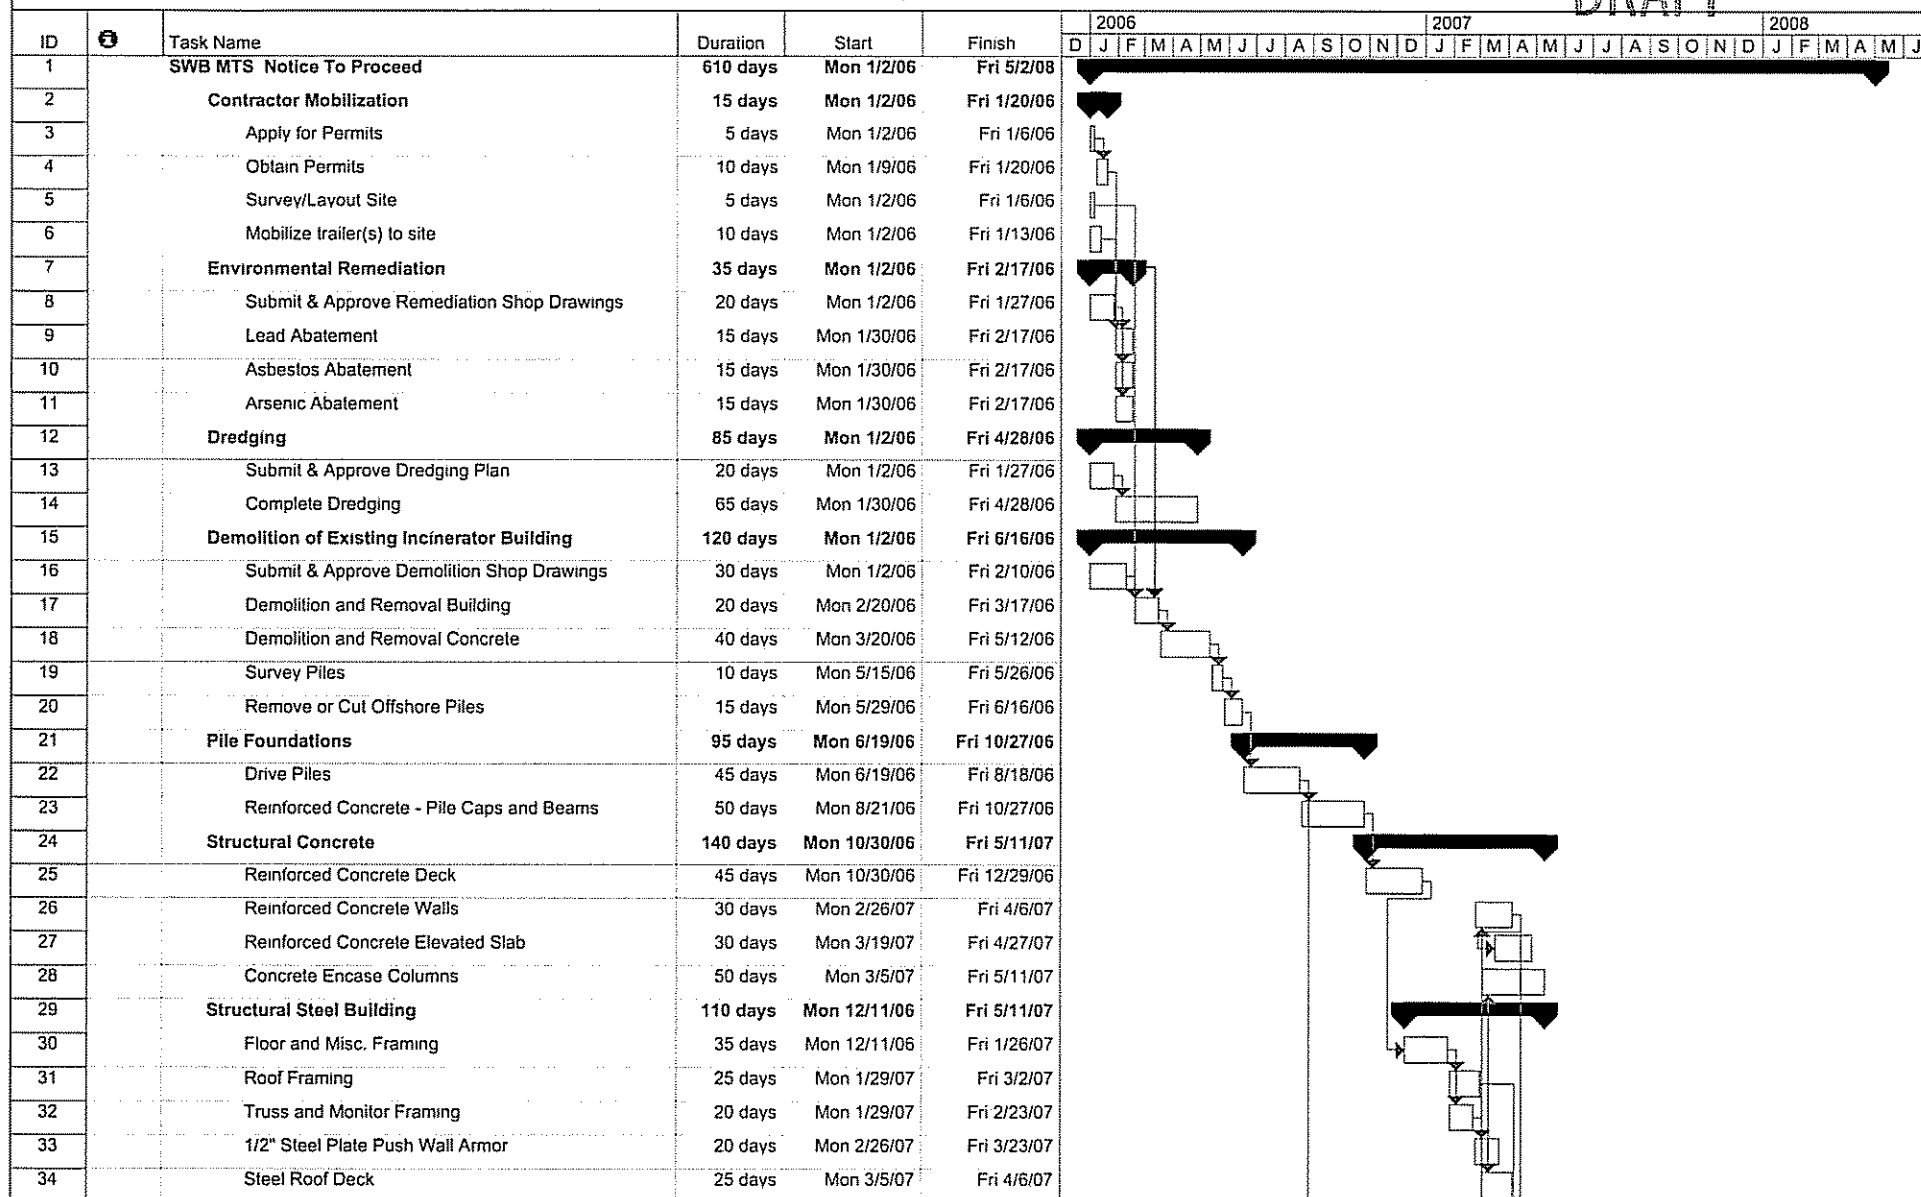

Project: Land MTS
Date: Tue 12/7/04

Task



Milestone



External Tasks



Split



Summary



External Milestone



Progress



Project Summary



Deadline



DRAFT

[illegible]

Project: Land MTS
Date: Tue 12/7/04

4

PRELIMINARY
DRAFT


Page 1

PRELIMINARY
DRAFT

Page 2

North Shore Marine Transfer Station

PRELIMINARY
DRAFT

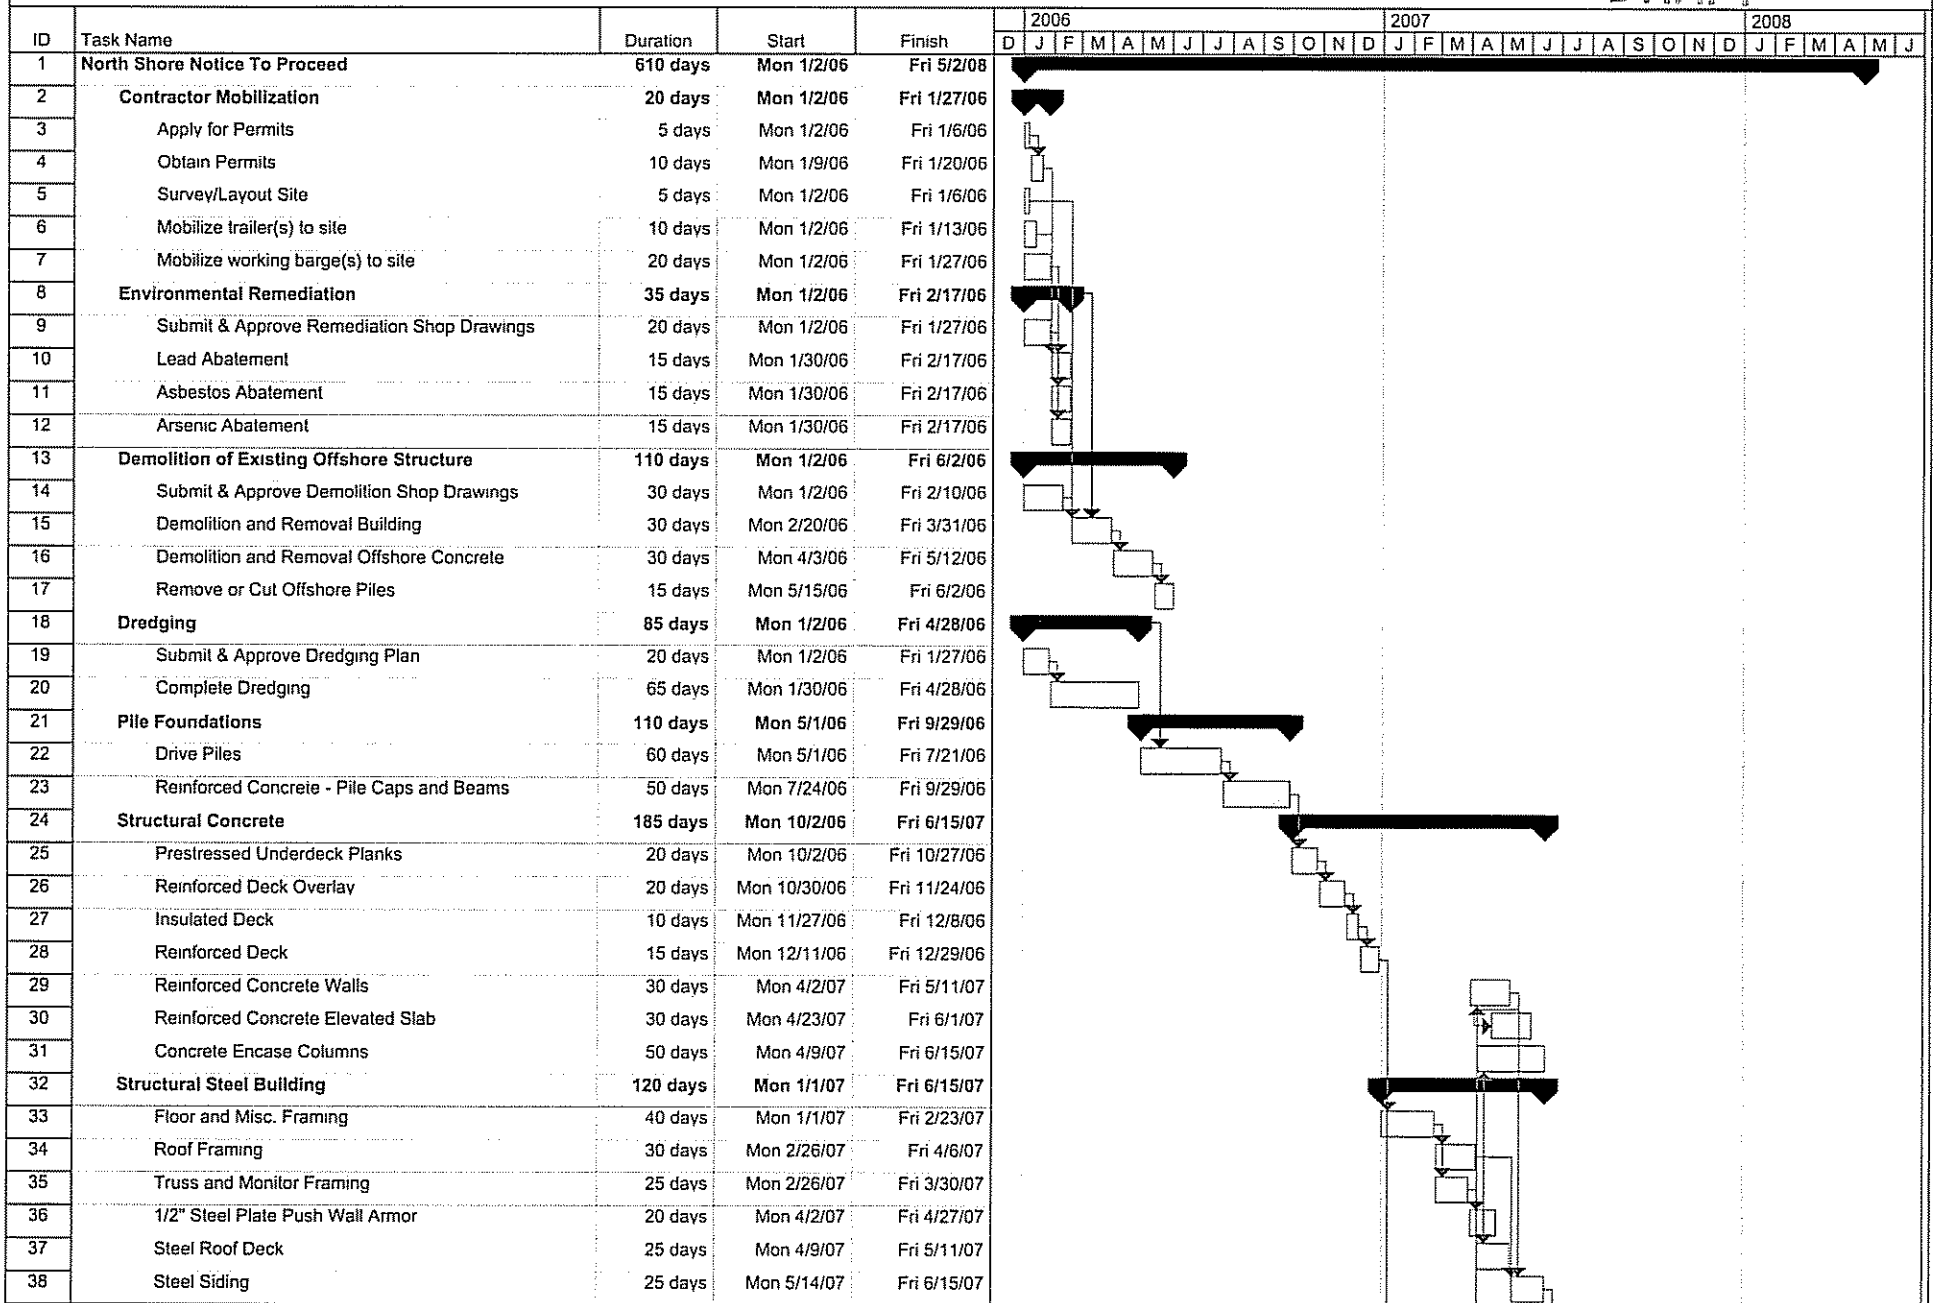

North Shore Marine Transfer Station

[illegible]
